

Status of Interconnect Works in the LHC Arcs and DS regions – week 8 (February 19 – 24, 2007)

C. Vollinger, AT-MCS (on behalf of the arc coordination team)


EDMS no. 823184

This report gives the status of the interconnect works in the LHC arcs and dispersion suppressor regions carried out during week 8 (February 19 - 24, 2007) in responsibility of the interconnection arc coordination team, starting with a general overview about the advancement per sector.

For the status of the VAC test, production rates, work progress, and number of operations foreseen and performed, the data is reported for each sector separately.

The Dashboard

- Number of magnets in the tunnel: 1162 MB, 447 SSS, 101 LSS.

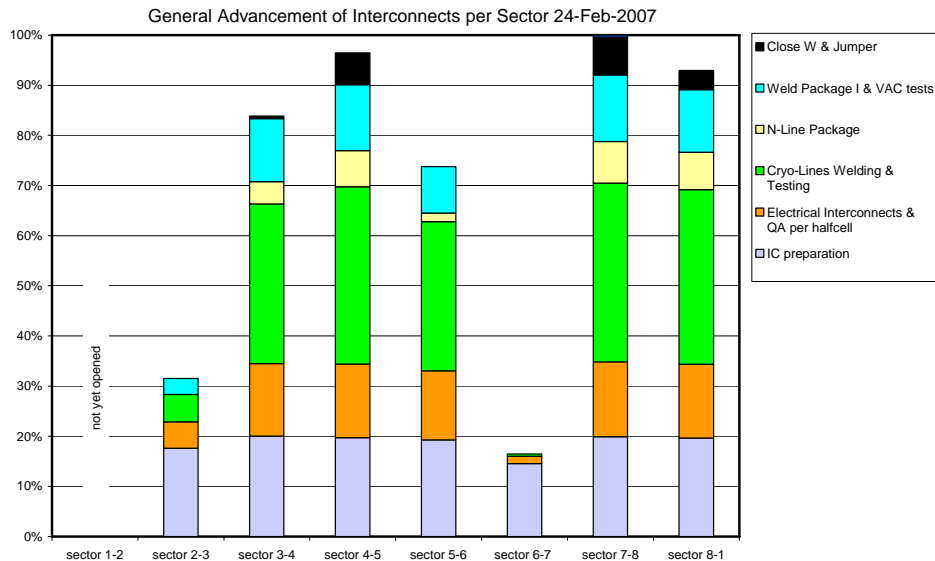

Data for General Advancement Plot is counted by number of interventions and grouped by activities as follows:

- IC preparation: Magnet alignment, IC pre-inspection, IC released for work,
- Electrical Interconnects & QA per halfcell: PAQ, US weld of spool pieces, brazing of main busbars,
- Cryo-Lines Welding & Testing: Welding of main busbar lines M1, M2, M3, weld K1 line, K2 line, K3 line, C' line, X line. Vacuum tests of K lines, C' line, X line.
- N-Line package: Insert N line, AIV 1, AIV 2, US welding of N line, weld of large sleeve for N line.
- Beam Pipes Welding & VAC tests. VAC sector test: Welding of V1, V2, E line and VAC tests V1, V2, E line. RF test magnet chain.
- Close W bellow and Jumper.
- VAC test for sector.

Sector coordination team:
P. Fessia, A. Musso, F. Seyvet, M. Struik, C. Vollinger

<i>Sectors</i>	<i>Started</i>
1-2	No
7-8	finished
2-3 3-4 4-5 5-6 6-7 8-1	Yes

Sector 1-2: not yet started.

Remarks:

1. The color coding of the general advancement plot matches the color coding of the other plots (snapshot and production rates).
2. The plots of the production rates also show the average production rate (IC/week) foreseen for the sectors and the ultimate production rates for the ideal case.

Sector 2-3

- Mounting of PIMs (Plug-In-Modules) re-started.
- All installed magnets are aligned and pre-inspected.

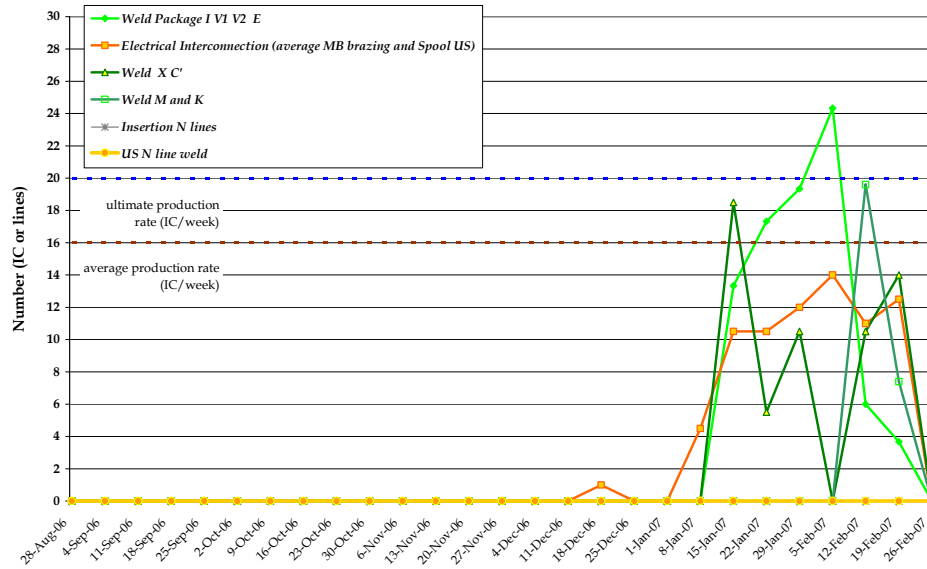


Fig. 1: Production rates in sector 2-3.

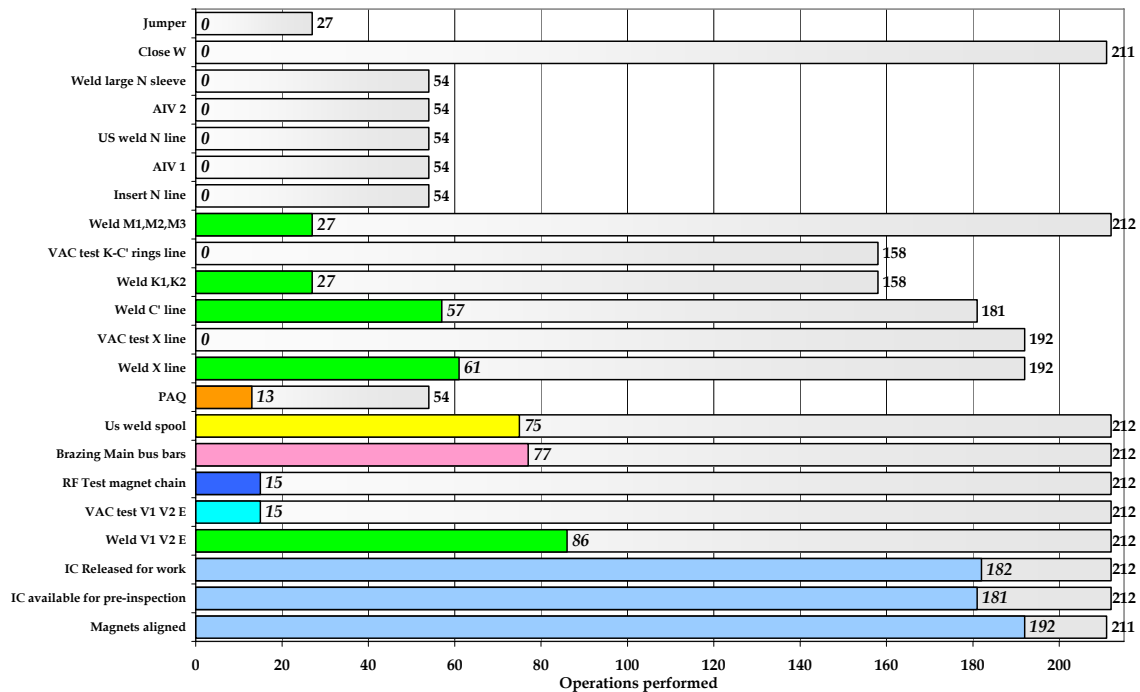


Fig. 2: Snapshot of work progress in sector 2-3 showing the number of operations achieved in total with respect to the total number of operations necessary.

Sector 3-4

- W-bellows of 1st 15 interconnections closed.

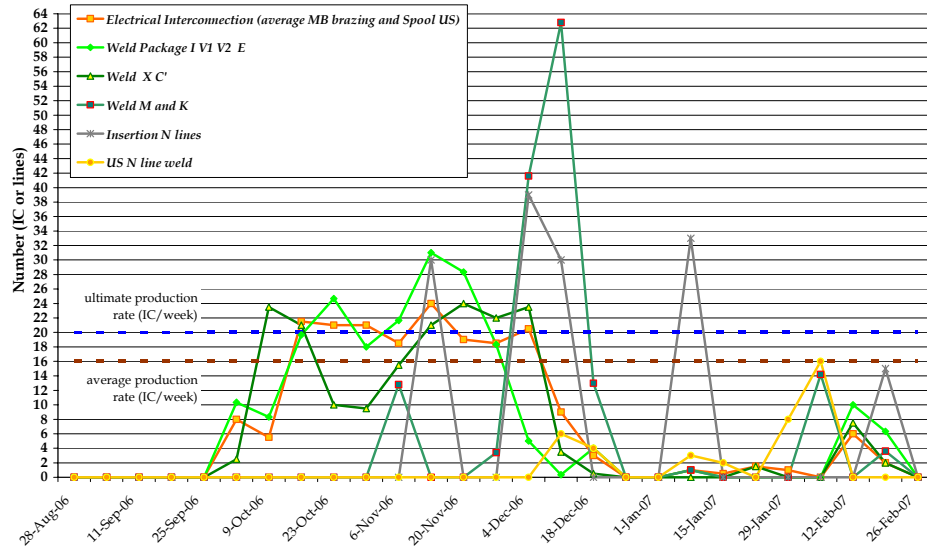


Fig. 3: Production rates in sector 3-4.

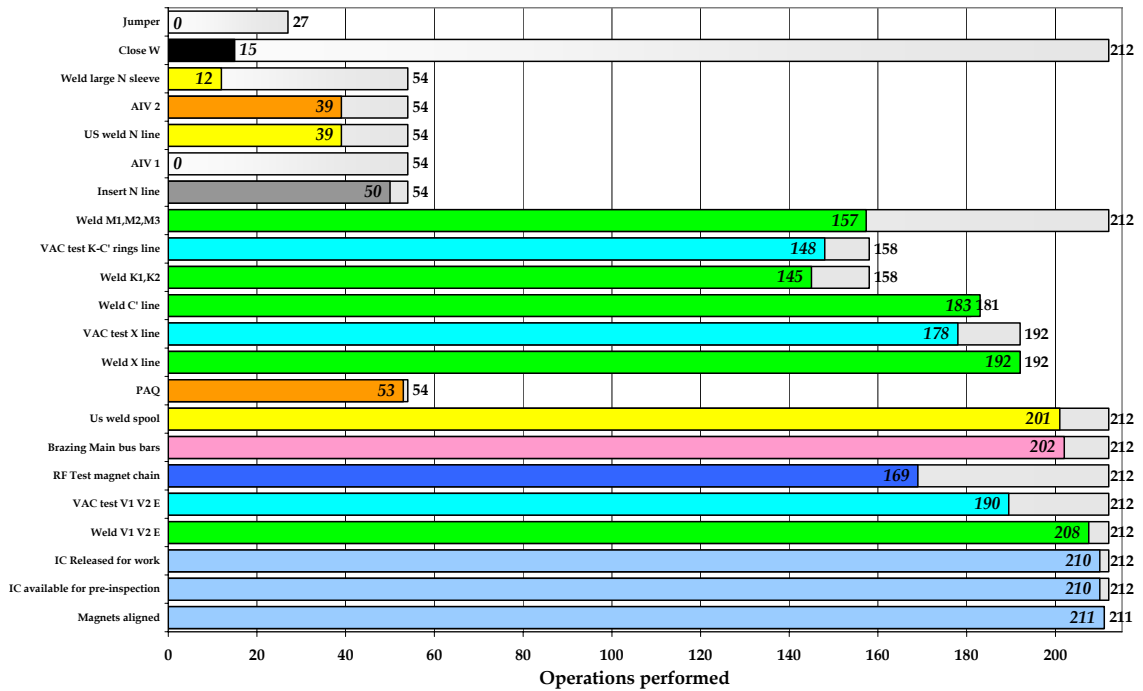


Fig. 4: Snapshot of work progress in sector 3-4 showing the number of operations achieved in total with respect to the total number of operations necessary.

Sector 4-5

- 3 vacuum sectors with leaks are repaired. Of these, 2 are already pumping, 1 to be closed next week. 2 other vacuum sectors tested.
- This way, all vacuum sectors not effected by the DS-regions are ready for test or testing.

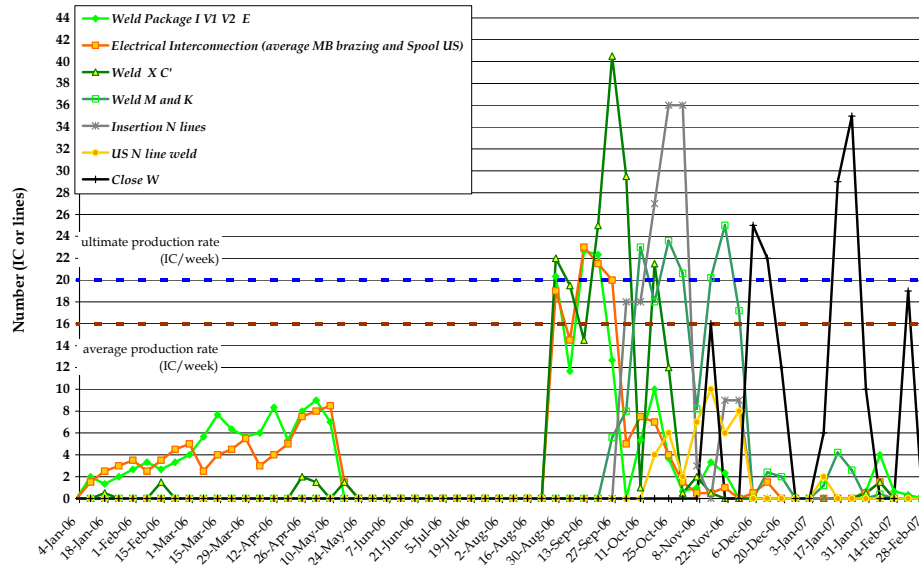


Fig. 5: Production rates in sector 4-5.

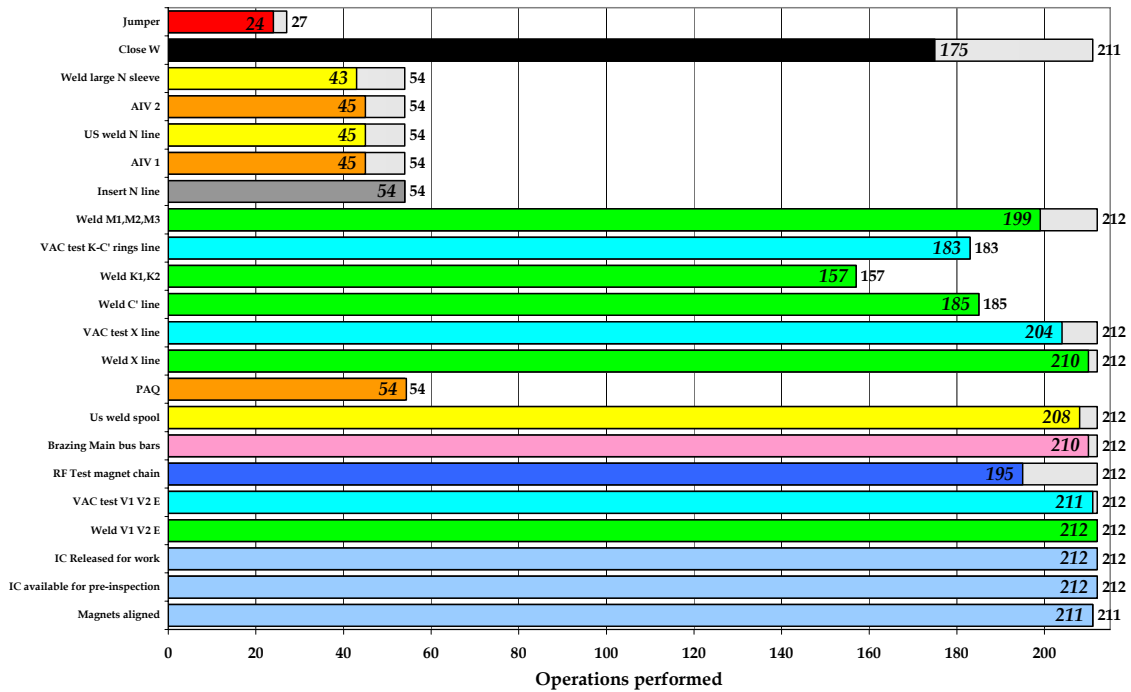


Fig. 6: Snapshot of work progress in sector 4-5 showing the number of operations achieved in total with respect to the total number of operations necessary.

Sector 5-6

- Nline inserted in R5.

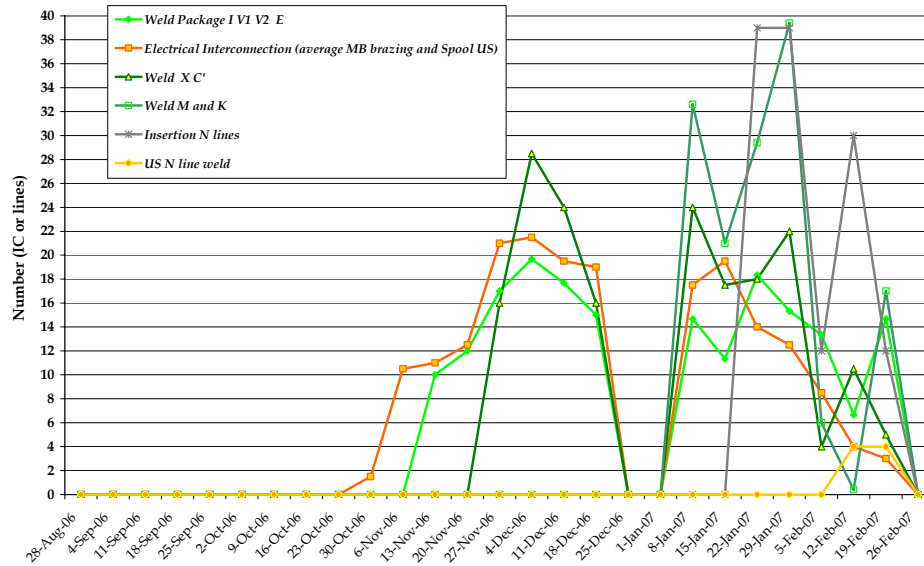


Fig. 7: Production rates in sector 5-6.

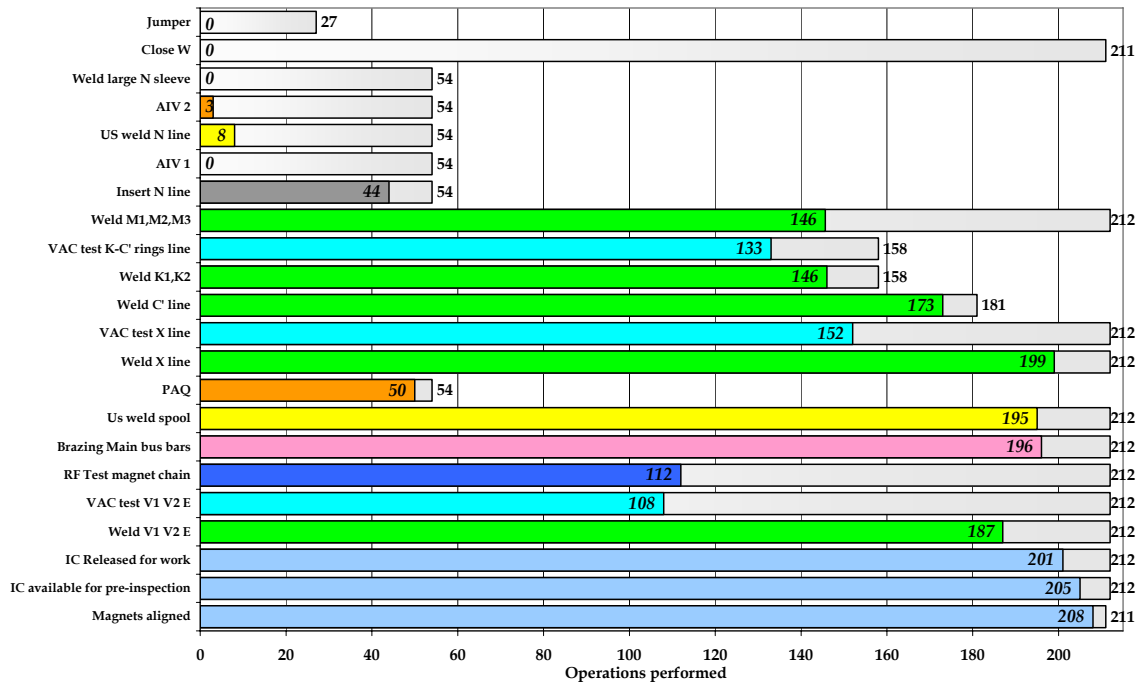


Fig. 8: Snapshot of work progress in sector 5-6 showing the number of operations achieved in total with respect to the total number of operations needed.

Sector 6-7

- 1st PAQ available for next week.

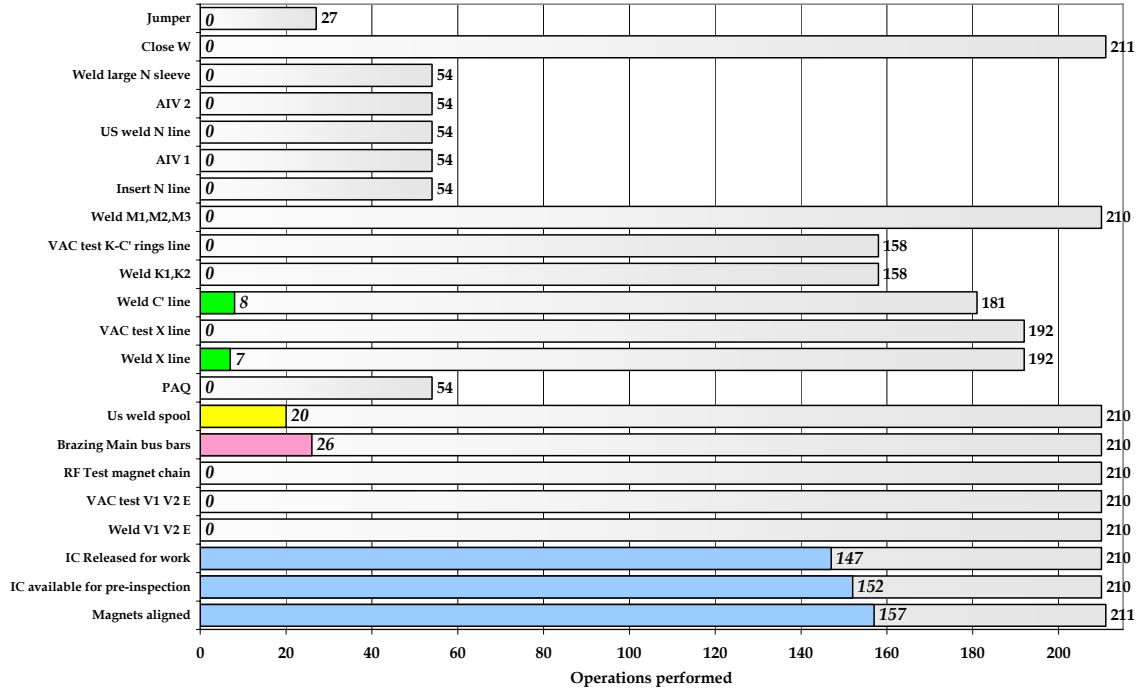


Fig. 9: Snapshot of work progress in sector 6-7 showing the number of operations achieved in total with respect to the total number of operations needed.

Sector 8-1

- Closing of W-bellows ongoing.
- NCR on DFBA closed.

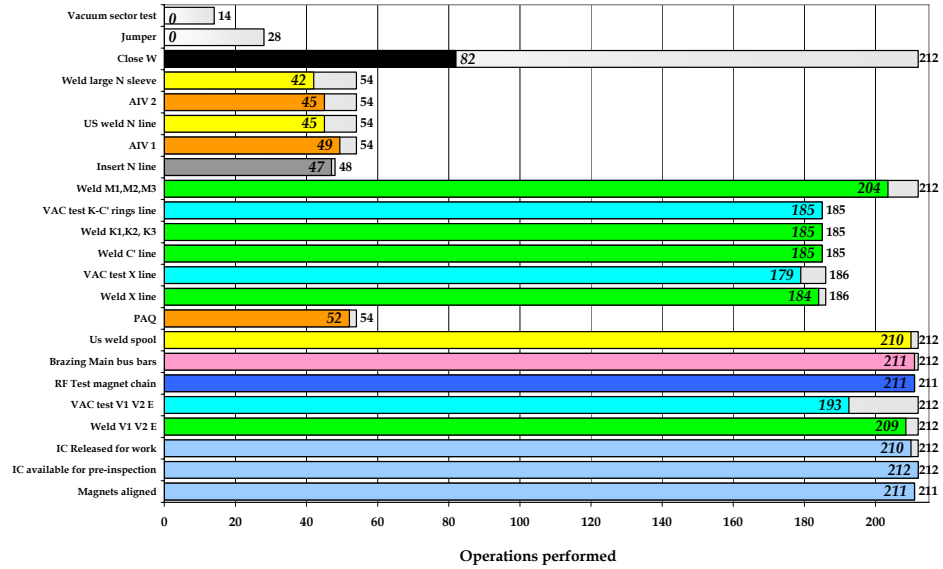


Fig. 10: Snapshot of work progress in sector 8-1 showing the number of operations achieved in total with respect to the total number of operations needed.

Vacuum Tests by Sector

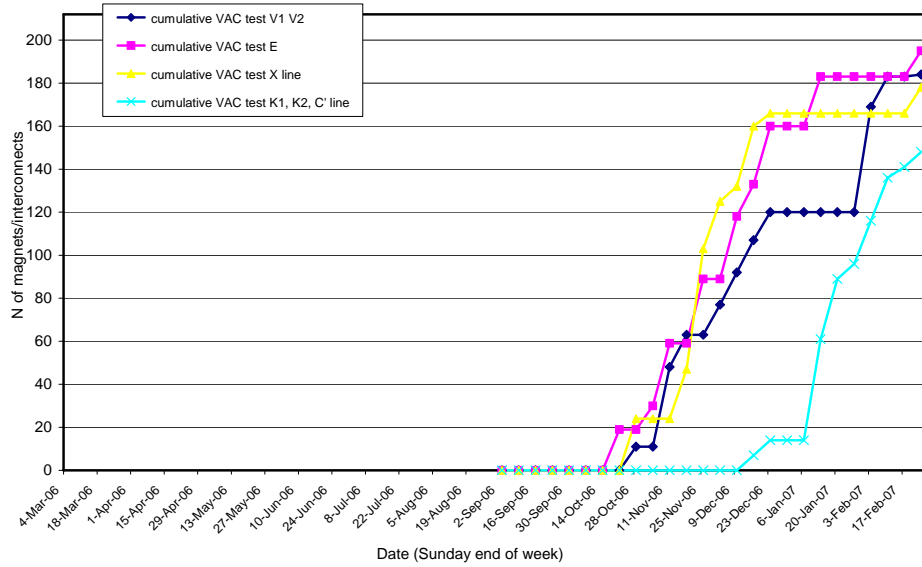


Fig. 11: Status of the VAC tests in sector 3-4.

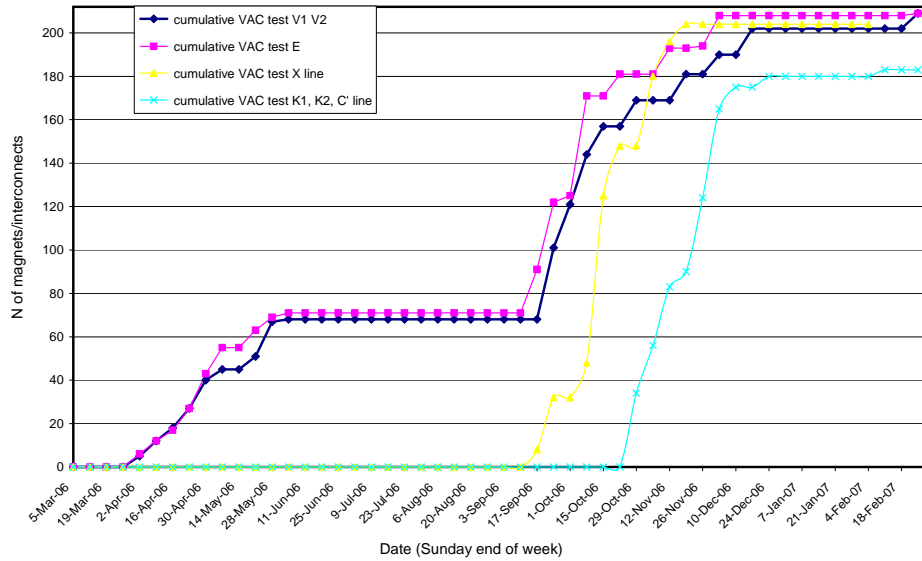


Fig. 12: Status of the VAC tests in sector 4-5.

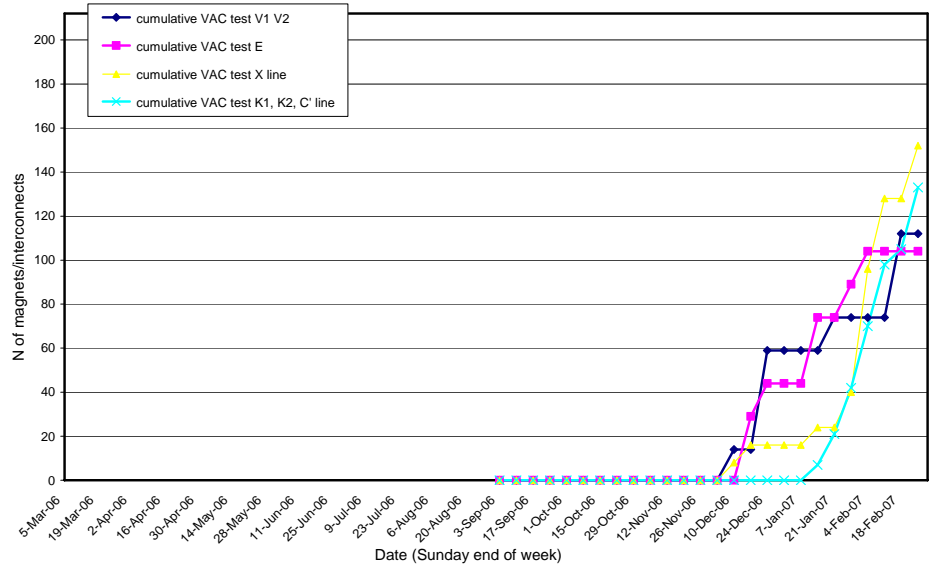


Fig. 13: Status of the VAC tests in sector 5-6.
